

Whole Program Report

Ohlone Community College District

Measure G

Reporting Period: Inception through 3/31/2017


Funding Sources (Budget)

Bond Authorization	\$349,000,000	99.52 %
Bond Allocated Interest Earned	\$644,293	0.18 %
Allocated Endowment Interest Earned	\$191,346	0.05 %
Unallocated Bond Interest Earned	\$741,443	0.21 %
Unallocated Endowment Interest Earned	\$115,353	0.03 %
<hr/>		
Total Bond:	\$350,692,435	100.00 %
State	\$0	0.00 %
Other	\$0	0.00 %
<hr/>		
Total Proceeds:	\$350,692,435	100.00 %

Cost Status

Category	Total Budget	Actual Expenses To Date			Remaining Balance
		Bond	State	Other	
A&E, Oversight, DSA & Other	\$47,481,543	\$31,430,403	\$0	\$0	\$16,051,140
Catastrophic Contingency	\$5,500,000	\$0	\$0	\$0	\$5,500,000
Construction & Contingency	\$262,910,323	\$118,701,777	\$0	\$0	\$144,208,545
Furniture & Equipment	\$17,369,053	\$5,122,933	\$0	\$0	\$12,246,120
Overhead	\$16,574,720	\$10,064,811	\$0	\$0	\$6,509,909
Unallocated Interest Earned	\$856,796	\$0	\$0	\$0	\$856,796
<hr/>					
Totals:	\$350,692,435	\$165,319,925	\$0	\$0	\$185,372,510

Budget vs Expenses (Bond Only)

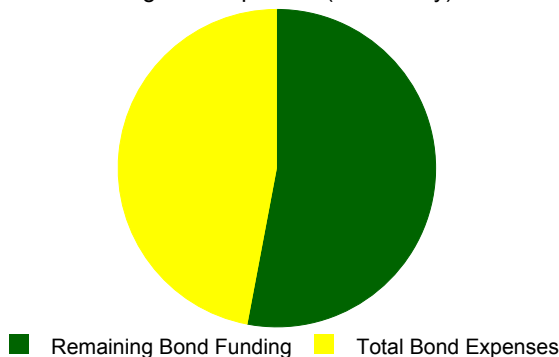

Notes:

Of the \$80 Million of Measure G Series A bond proceeds, \$10 Million has been placed in a Technology Endowment Fund to support future technology equipment purchases.

Bond and Bond Authorization: Measure G
 Interest Earned: Measure G Interest Earnings Allocated to Projects
 Endowment Interest Earned: Interest earnings on endowment allocated to specific endowment projects
 Unallocated Interest Earned: Interest Earnings not yet allocated to specific projects
 Unallocated Endowment Interest Earned: Interest earnings not yet allocated to specific endowment projects
 State: State Capital Outlay and Scheduled Maintenance (only on Measure G projects)
 Other: Contribution to Project from "other" source (non-State nor Bond)
 Expenses in the "Actual Expenses to Date" columns: Paid and Accrued expenses through the reporting period end date
 Rounding factors may apply

CBOC Quarterly Summary Report

Ohlone Community College District

Measure G Bond Program

Reporting Period: Inception through 3/31/2017

Phase/Project Name		Bond Budget	Bond Exp. To Date	Qtr Bond Expense	Budget Remaining
Project List					
Phases					
Board Approved					
6138	Campus Way-finding Signage	\$452,360	\$0	\$0	\$452,360
6139	Campus Entry Improvements	\$595,600	\$0	\$0	\$595,600
6143	Small Capital Improvements	\$775,000	\$0	\$0	\$775,000
9111	Instructional Technology (Computers, LCDS, Flat Screens, etc) - (PH 2)	\$1,560,000	\$56,997	\$56,997	\$1,503,003
9113	Instructional Technology (Computers, LCDS, Flat Screens, etc) - (PH 3)	\$1,560,000	\$0	\$0	\$1,560,000
9114	FFE for Hyman Hall	\$1,000,000	\$0	\$0	\$1,000,000
Total Board Approved		\$5,942,960	\$56,997	\$56,997	\$5,885,963
Programming					
6109	Plaza & Landscape Improvements	\$1,000,000	\$268,454	\$0	\$731,546
6121	Renovate Building 9	\$11,050,920	\$3,480,036	\$12,730	\$7,570,883
6142	Hyman Hall Renovations	\$5,301,726	\$1,392,959	\$0	\$3,908,767
9116	FFE for Building 5	\$1,000,000	\$8,075	\$0	\$991,925
9117	FFE for Building 9	\$600,000	\$66,454	\$0	\$533,546
9999	Program Mgmt, Planning and Support	\$9,800,279	\$2,491,683	\$379,909	\$7,308,596
Total Programming		\$28,752,924	\$7,707,661	\$392,639	\$21,045,263
Design					
6110	Parking Structures	\$31,865,970	\$25,731,968	\$5,840	\$6,134,002
6114	Renovate Building 5	\$6,438,146	\$56,726	\$0	\$6,381,420
6131	Site Lighting Upgrades	\$675,000	\$75,626	\$34,373	\$599,374
9106	FFE for Academic Core Project	\$7,587,355	\$417,407	\$109,644	\$7,169,948
Total Design		\$46,566,470	\$26,281,727	\$149,858	\$20,284,744
Construction					
6105	Academic Core Buildings	\$180,346,965	\$61,425,931	\$10,614,497	\$118,921,034
6108	Parking, Road and Site Improvements	\$1,799,449	\$960,539	\$286,816	\$838,910
6134	Site Security Systems	\$1,418,358	\$441,478	\$235,892	\$976,880
9101	Renewable Energy Generation	\$32,106,082	\$25,441,904	\$2,194,635	\$6,664,178
9107	Quick Fix: Imminent Failure	\$4,856,658	\$4,785,060	\$81,984	\$71,597
9108	Quick Fix: Safety and Accessibility	\$2,609,553	\$2,555,581	\$48,476	\$53,972
9109	Quick Fix: Way-finding and Landscape	\$313,591	\$238,353	\$3,315	\$75,238
Total Construction		\$223,450,656	\$95,848,847	\$13,465,613	\$127,601,809
Close Out					
6101	Athletic Fields	\$14,197,108	\$13,157,205	\$18,338	\$1,039,903
6102	Roof Repair/Replacement	\$1,050,165	\$908,950	\$26,179	\$141,216
9112	FFE for Athletic Fields	\$400,000	\$358,710	(\$944)	\$41,290
Total Close Out		\$15,647,274	\$14,424,865	\$43,573	\$1,222,409
Procurement					

Notes:

Expenses in the "Bond Exp. to Date" column include expenses paid and accrued through the reporting period end date. Rounding factors may apply.

CBOC Quarterly Summary Report

Ohlone Community College District

Measure G Bond Program

Reporting Period: Inception through 3/31/2017

Phase/Project Name	Bond Budget	Bond Exp. To Date	Qtr Bond Expense	Budget Remaining
9104 Information Technology Infrastructure Upgrades	\$2,275,000	\$2,261,445	\$0	\$13,555
9105 Instructional Technology (Computers, LCDS, Flat Screens, etc) - (PH 1)	\$1,503,031	\$1,493,944	\$0	\$9,087
Total Procurement	\$3,778,031	\$3,755,388	\$0	\$22,643
Complete				
6104 Site Utility Infrastructure Improvements	\$13,678,562	\$13,678,562	\$0	\$0
6133 Bird (Swallow) Environmental Alternatives	\$283,904	\$283,904	\$0	\$0
7102 Newark Additional Parking (300 spaces)	\$884,911	\$884,911	\$0	\$0
7105 Newark Greenhouse Project	\$383,105	\$383,105	\$0	\$0
9115 Energy Efficiency Projects	\$17,286	\$17,286	\$0	\$0
Total Complete	\$15,247,767	\$15,247,767	\$0	\$0
Consolidated				
6103 Field House	\$0	\$0	\$0	\$0
6106 Renovate Building 1	\$0	\$0	\$0	\$0
6107 New Parking Lot L	\$0	\$0	\$0	\$0
6111 "Main Street" Improvements -- South Side	\$0	\$0	\$0	\$0
6112 Hillside Image and Accessibility Improvements (PH 1)	\$0	\$0	\$0	\$0
6113 Hillside Image and Accessibility Improvements (PH 2)	\$0	\$0	\$0	\$0
6115 Relocate Soccer Field	\$0	\$0	\$0	\$0
6116 Multipurpose Soccer Practice Field	\$0	\$0	\$0	\$0
6117 Open Anza Pine Road at Hillside:	\$0	\$0	\$0	\$0
6118 Construct North/South Road Behind Mission Boulevard Frontage Development	\$0	\$0	\$0	\$0
6119 Softball Field Improvements	\$0	\$0	\$0	\$0
6120 Soccer/Softball Field House	\$0	\$0	\$0	\$0
6122 Hillside Image and Accessibility Improvements (PH 3)	\$0	\$0	\$0	\$0
6123 New Building E	\$0	\$0	\$0	\$0
6124 "Library Plaza" Improvements -- North Side	\$0	\$0	\$0	\$0
6125 North Parking Structure	\$0	\$0	\$0	\$0
6126 Building 3 and 4 Replacement	\$0	\$0	\$0	\$0
6127 "Main Street" Improvements -- North Side	\$0	\$0	\$0	\$0
6128 Café/Event/Drop Off Structure	\$0	\$0	\$0	\$0
6129 Road Repair, Resurfacing and Replacement	\$0	\$0	\$0	\$0
6130 Roof Replacement Bldgs 12, 19, and 22	\$0	\$0	\$0	\$0
6132 Hazardous Material Abatement and Removal	\$0	\$0	\$0	\$0
6135 Sidewalk, Ramp and Plaza Repairs/Replacement	\$0	\$0	\$0	\$0
6136 Enhance environment around the upper pond	\$0	\$0	\$0	\$0
6137 Wetland Living/Learning Environment	\$0	\$0	\$0	\$0
6140 Campus-Wide Landscape Repairs and Upgrades, Tree Removal and Replacement, Erosion Control	\$0	\$0	\$0	\$0
6141 Bus Stop Concrete "Skid" Pads	\$0	\$0	\$0	\$0
7101 Newark Loop Roadway Improvements	\$0	\$0	\$0	\$0
7103 Newark Soil Remediation	\$0	\$0	\$0	\$0

Notes:

Expenses in the "Bond Exp. to Date" column include expenses paid and accrued through the reporting period end date. Rounding factors may apply.

CBOC Quarterly Summary Report

Ohlone Community College District

Measure G Bond Program

Reporting Period: Inception through 3/31/2017

Phase/Project Name		Bond Budget	Bond Exp. To Date	Qtr Bond Expense	Budget Remaining
7104	Newark Maintenance/Warehouse Building	\$0	\$0	\$0	\$0
9102	Newark Renewable Energy Generation	\$0	\$0	\$0	\$0
9103	Renewable Energy Generation (PH 2)	\$0	\$0	\$0	\$0
9110	Planning Assessments and Program Management	\$0	\$0	\$0	\$0
CIDSPM	Contingency, Inflation, District Support & Project Mgmt	\$0	\$0	\$0	\$0
Total Consolidated		\$0	\$0	\$0	\$0
Ohlone College Totals		\$339,386,082	\$163,323,251	\$14,108,680	\$176,062,830
Unallocated Interest Earnings		\$856,796	\$0	\$0	\$856,796
Measure G Project List Subtotal:		\$340,242,878	\$163,323,251	\$14,108,680	\$176,919,626
Contingency					
9500	Catastrophic Contingency	\$5,500,000	\$0	\$0	\$5,500,000
9600	Program Contingency	\$4,949,557	\$1,996,673	(\$4,538)	\$2,952,884
Total Contingency		\$10,449,557	\$1,996,673	(\$4,538)	\$8,452,884
Ohlone Contingency / (Forecasted Total Cost - Expenses to Date)					5.6%
Measure G Project List Total:		\$350,692,434	\$165,319,925	\$14,104,142	\$185,372,510

Notes:

Expenses in the "Bond Exp. to Date" column include expenses paid and accrued through the reporting period end date. Rounding factors may apply.
